
Three towns within one whole-site structure

Three conditional settlements; separate production; fixed pilots preserved; the whole issued boundary remains the planning extent.

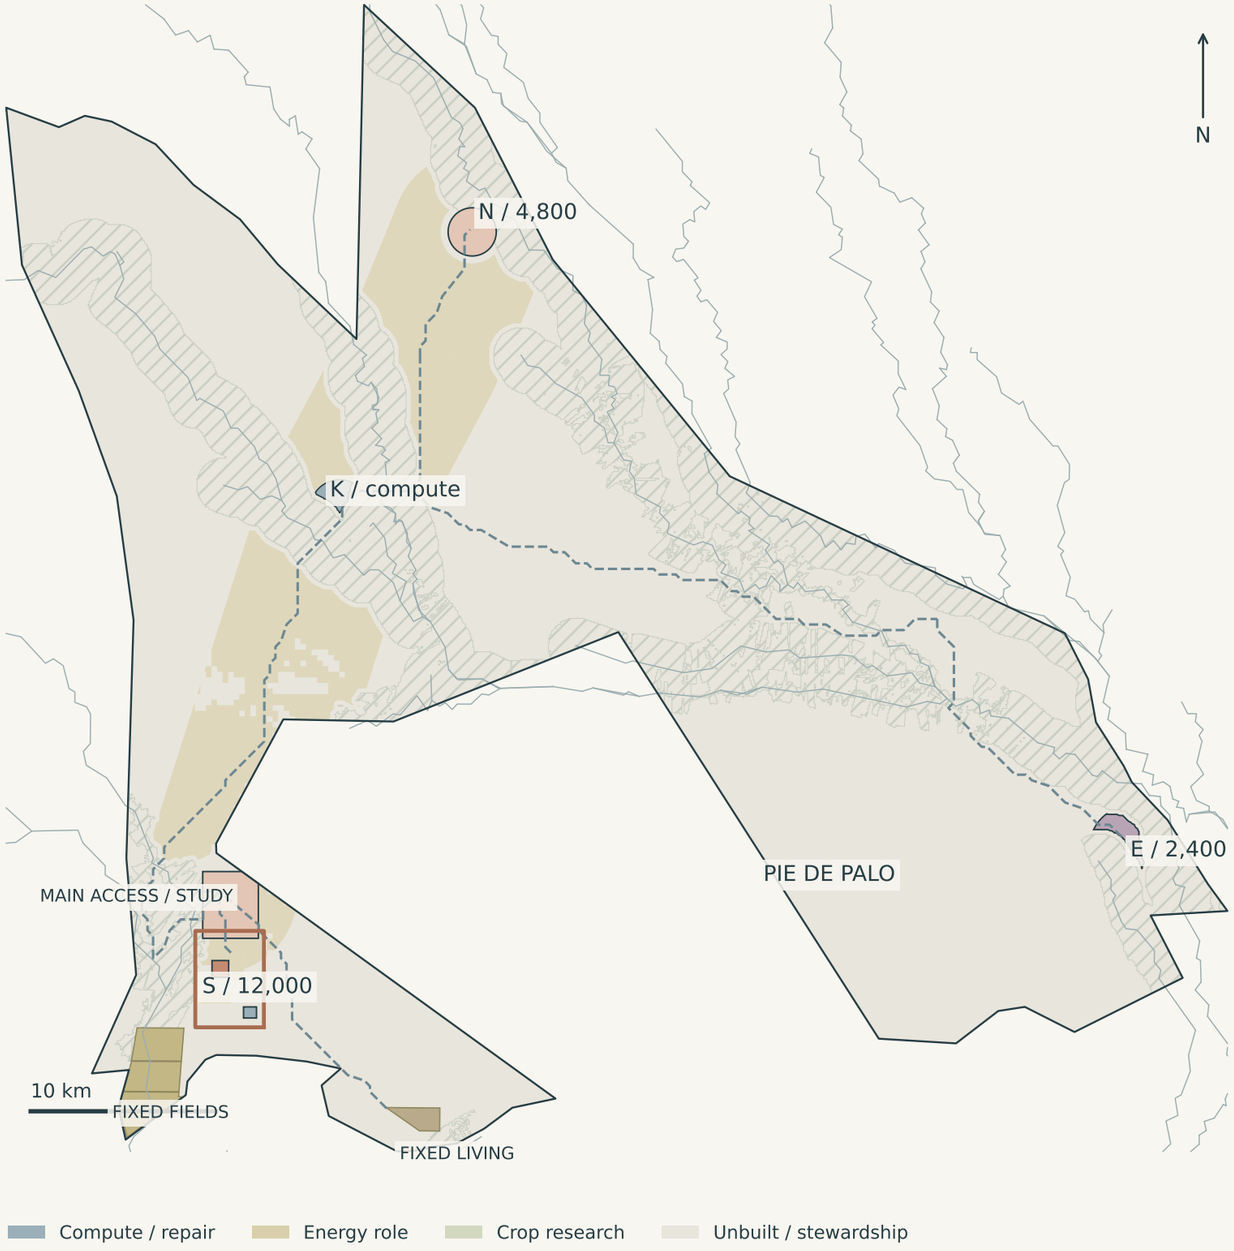

Dashed corridors are studies. RN40 approach and external rights remain unresolved enabling works; no secured water is inferred.

S / first town, then contiguous growth

960 dwellings / 2,400 new residents in Phase 1. Grow this town before launching remote settlements. Ultimate 12,000 is a conditional programme, not existing stock.

N / northern service town

Phase 3 only: up to 4,800 residents with its own water, school, care and local production. No dependence on daily travel to the first town.

E / gateway settlement


Phase 3 only: up to 2,400 residents serving logistics and gateway industry. Regional corridor, water and trade status are separate go/no-go tests.

The land between towns has a role

Conditional energy and crop research, channel conveyance and mountain/open-ground stewardship. Hatching is flood screening, not a lake or a blanket permanent no-build zone.

Five boundaries with five different jobs

Whole site / design study / actual Phase 1 / urban-design enlargement / three nodes and their camera crops are separate.

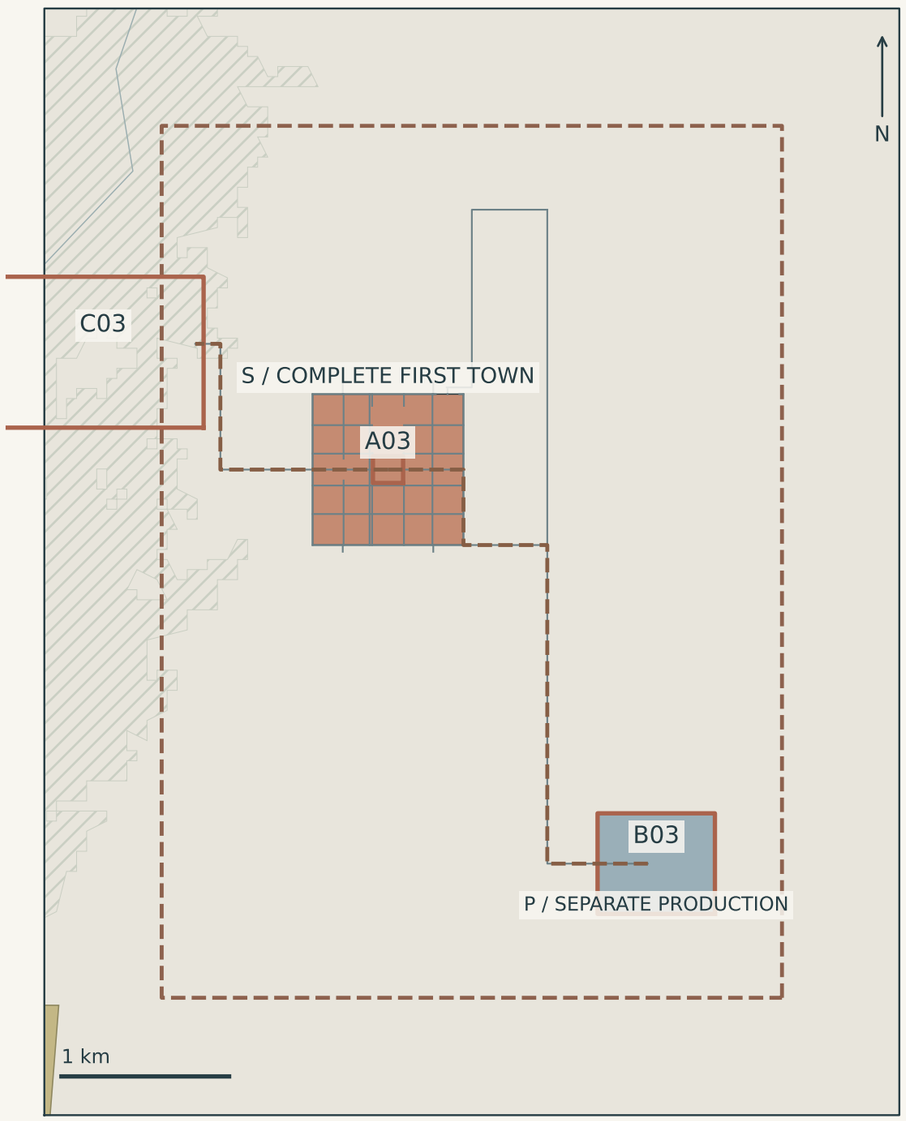

Study is not construction

19.24 km2 design-study rectangle. First-town gross extent 0.81 km2; production plot 0.42 km2. Corridors and park works are separate quantities.

B03 moves away from housing

Nearest proposed home-to-compute footprint gap: 2,268 m. Commons-to-campus route: 3.90 km. These are geometry distances, not acoustic or traffic compliance.

C03 is genuinely elsewhere


Park access from the commons follows a 1.90 km proposed route. High-ground entry, no permanent building in the channel; access closes on warning.

Retired shortcut

No long heat pipe is proposed to the town. Heat reuse receives zero credit until a real nearby receiver, temperatures, seasonal demand and economics are verified.

The first town is a complete spatial unit

Sixteen blocks / 960 dwellings / 2,400 residents at 2.5 people per dwelling / three storeys. All are design scenarios.

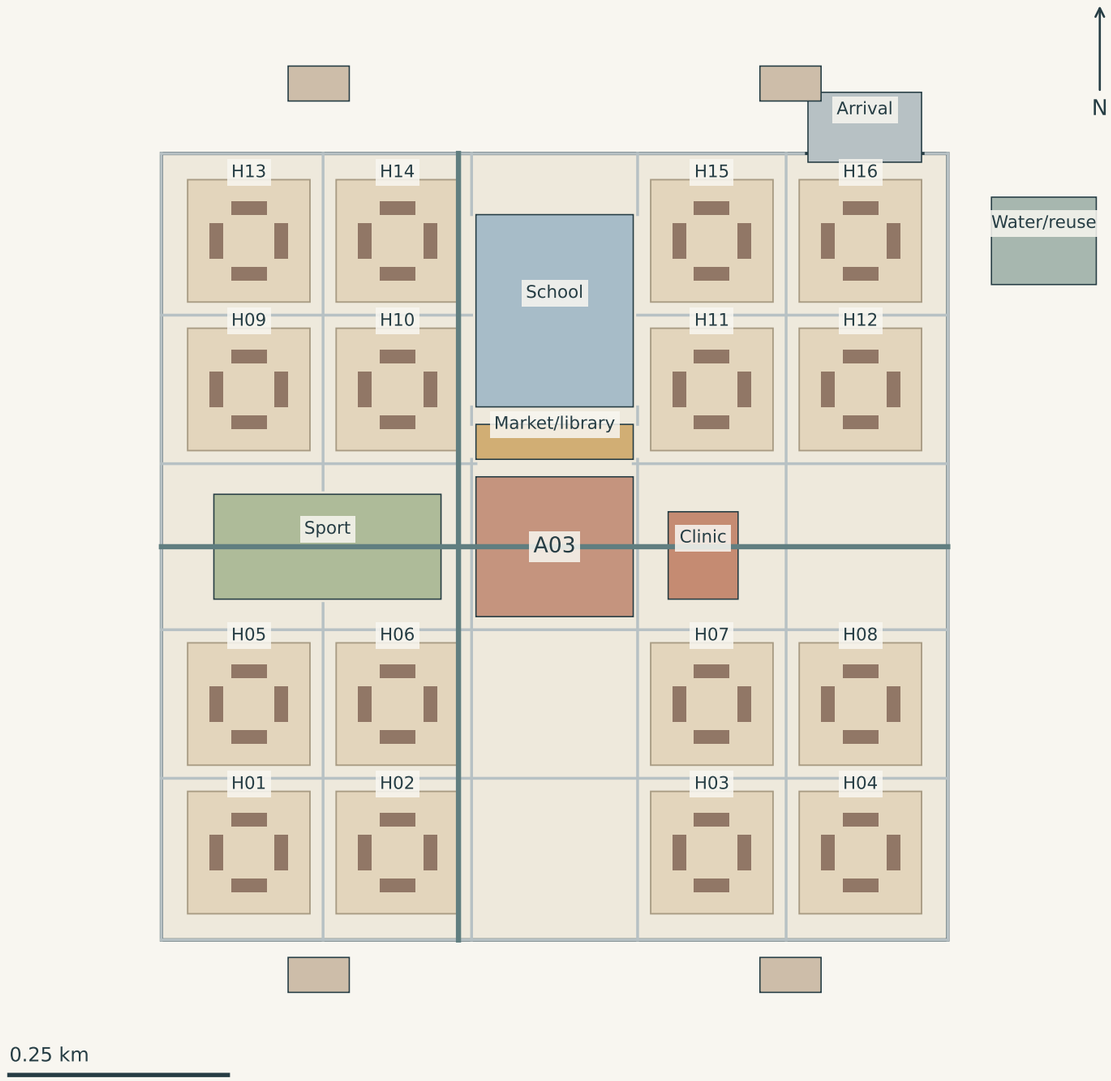

Homes form four neighbourhoods

Each neighbourhood has four 60-dwelling blocks and local care. Four 15-dwelling buildings define each shared court; 64 buildings total. Housing GFA 115,200 m2; average 120 m2 per dwelling includes common circulation.

The civic cross comes first

One central school/shared-sport plot, primary care, market/library, water/reuse, passenger arrival and four local care plots. School capacity scenario: 360 places, from 15% of 2,400 residents; demographic model to verify.

Walking is a network

Continuous street grid plus civic and cross-town walking routes. Farther homes need measured safe routes and accessible shuttle service; no untested five-minute-city claim.


Land outside the blocks is explicit

Public streets, care/service plots, the dry civic cross and unbuilt desert ground. The latter is neither irrigated landscape nor an excuse to count empty land as designed housing.

Three nodes test three city promises

Each node has its own place, users, access, operating rule and design question. Local images will be labelled with their actual extent.

A03 / Climate commons

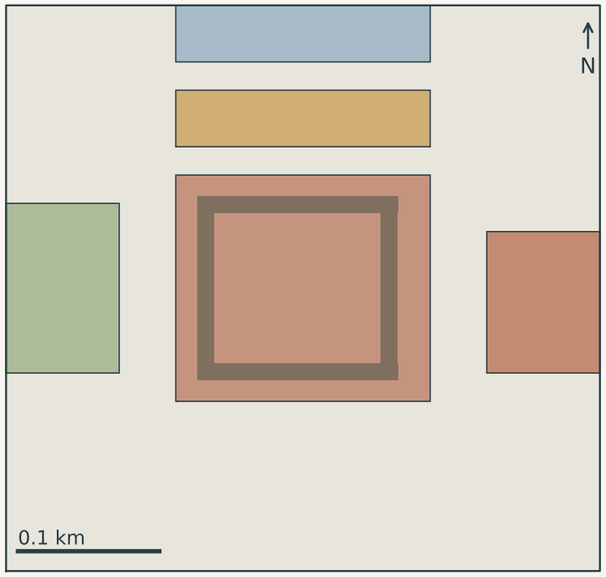


People before the heat

180 x 160 m climate commons, with deep perimeter shade, public drinking water and a nearby cooled refuge. Children, older people and shift workers have step-free entry. Shade geometry and structural/seismic design still require seasonal checks.

STATUS / Proposed geometry and operating intent.
Finished views must be regenerated from this changed geometry.

B03 / Compute with a water stop-rule

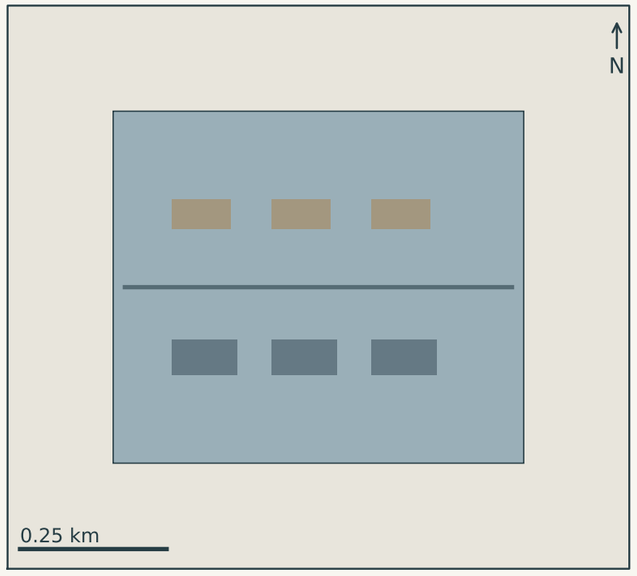


Production accepts limits

Three 2 MW hall scenarios, service spine and repair plots. Dry cooling, noise/dust monitoring and independent emergency access. No residential heat-network claim; local pilot receiver only after measured demand tests.

STATUS / Proposed geometry and operating intent.
Finished views must be regenerated from this changed geometry.

C03 / Seasonal wash park

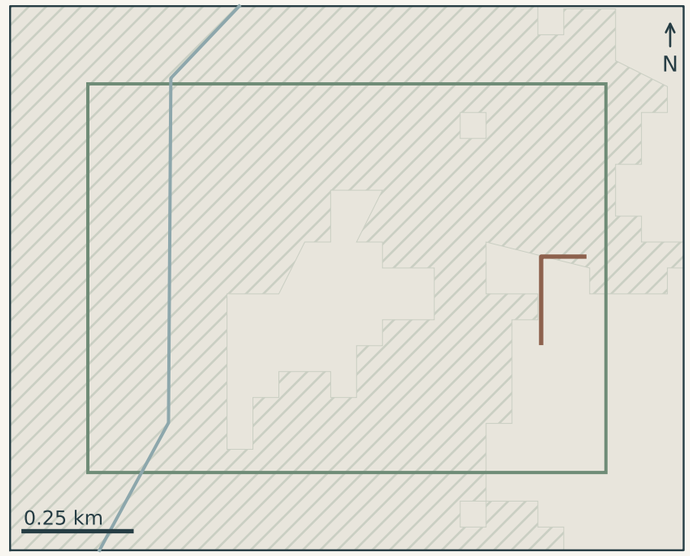

The channel stays a channel

Seasonal wash plus a removable, high-ground visiting route. No ornamental lake, no occupied pavilion on the flow line and no invented retention dam. Storm warning closes the lower route; a hydraulic study defines the actual safe edge.

STATUS / Proposed geometry and operating intent.
Finished views must be regenerated from this changed geometry.

Construction follows a capacity ledger

Relative timing is a scenario; every remote settlement must pass its own resource and service tests.

Phase	New residents	Total residents	New homes	Total homes	New jobs	Total jobs
1	2400	2400	960	960	1200	1200
2	4800	7200	1920	2880	2800	4000
3	12000	19200	4800	7680	5600	9600

PHASE 1

Scenario years 0-4 after enabling conditions

One operable town plus separate production

Survey, lawful source and external access before occupancy / First housing, care, school, clinic, storage, reuse and public transport / Separate production gates; trial crops only outside fixed pilots

START ONLY WHEN

Lawful source passes quantity/quality tests; full pilot demand audited; access and service operations funded

PHASE 2

Scenario years 4-8; may never start

Expand the existing town before another settlement

Expand school and health capacity with housing / Extend source/renewables only with permits and demand / Conditional central compute campus has its own services

START ONLY WHEN

80% occupancy and 12 months of audited source headroom after all fixed and new uses; committed jobs and public services

PHASE 3

Scenario years 8-15+; separate go/no-go decisions

Conditional northern town and eastern gateway

Independent services at each settlement / Surveyed regional corridor and emergency alternatives / Gateway supply/receiving works and customs status before terminal construction


START ONLY WHEN

Each remote location passes its own water, power, access, demand and service tests; gateway has lawful trade status

S: south-west town / P: local production / K: central compute / N: north town / E: eastern gateway settlement. All jobs are uncontracted programme targets.

Water sets the construction threshold

Incremental new-development model only. Fixed pilot and living-quarter demand remain unknown and must be added before any supply claim.

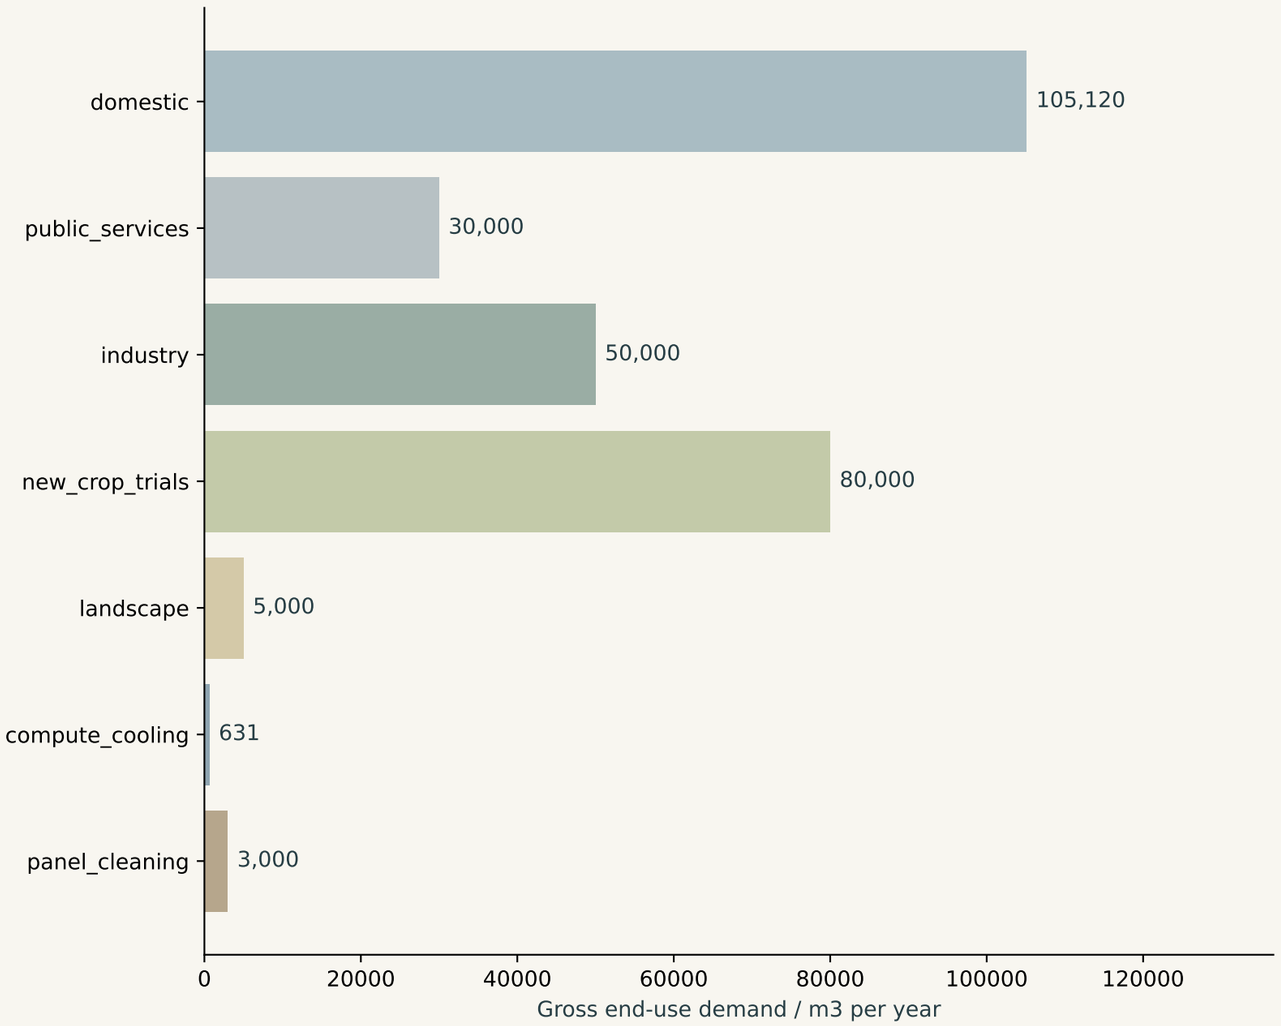

Demand comes before an assumed supply

Gross new demand 273,751 m3/year. Reclaimed substitution 75,000; source requirement 220,834 with 10% distribution loss. This is a requirement to secure, not a well yield or entitlement.

Cooling does not buy adjacency

6 MW peak IT, 60% annual utilisation and 0.02 L/kWh cooling WUE are scenario inputs. Imported electricity gets no unverified carbon-free credit. No hourly carbon-free percentage is carried over from the old 12 MW model.

A 30% shortage changes operation

Protect safe drinking water, care and wastewater treatment. Curtail new crop trials and nonessential industry first; interrupt compute and discretionary cleaning. Fixed-pilot obligations require operator agreement and cannot be silently subordinated.

Under the arrays: forage grass and jojoba only. This draft neither reallocates the fixed fields nor invents their irrigation demand.
No occupancy gate clears until the combined existing + new supply balance is independently verified.

What is corrected, what remains unproven

Independent content audit / not an organiser assessment / automatic gate success is not a design approval.

CORRECTED / Extents

A new 19.24 km2 study is separate from the 0.81 km2 first town and 0.42 km2 production plot. The entire issued site remains the structural planning extent.

CORRECTED / Facilities

Compute moved to a separate access-controlled plot. Distances are computed from candidate geometry; no heat-reuse percentage is assumed.

CORRECTED / Phasing

A zone-by-zone draft records new/cumulative people, dwellings and jobs. Phase 3 is conditional; future settlement blocks have not been claimed as already detailed.

SOURCE CONFLICT / Boundary

The boundary revision says 1,658.819819 km2 after the authorised open-seam closure. Some narrative site text still repeats the older internal-seam-only account. V7 uses the current geometry + revision record; nominal 1,656 remains the project label.

REQUIRED / Engineering and livelihood

Water source, combined pilot demand, external road rights, crossings, seismic structure, dust/noise, school demographics and job demand need verification. A 60 m terrain cell cannot certify a building plot.

REQUIRED / Submission and images

This review does not replace the published seven geometry files or assert a new 12/12. Core package integration, matrix reconciliation, camera/control generation and finished-image QA follow the planning review. Older images do not illustrate the changed production location.

PRE-QA / 70 candidate buildings / 960 dwellings / overlap 0.0 m2 / hard-screen conflicts 0 / flood-screen intersections 0
